

# Infrastructure Upgrades along 2<sup>nd</sup> Avenue. & Surrounding Areas

## Murray Hill/Kips Bay Area

## Project #MED607

The New York City Department of Design and Construction (NYCDDC) continues to manage the \$37 million dollar capital construction Infrastructure Upgrade Project #MED607. Work includes, but is not limited to, the installation of catch basins at various locations, utility upgrades, limited sewer upgrades, new hydrant installation and the installation of new water main pipes in various locations. This project has an anticipated completion date of January 2025.



48" TWM Installation on E. 35<sup>th</sup> Street / QMT Approach

### Work Completed: Second Quarter 2023

Permanent restoration of E. 35<sup>th</sup> Street b/w 1<sup>st</sup> Ave. and 2<sup>nd</sup> Ave. Permanent restoration on 2<sup>nd</sup> Ave. b/w E. 32<sup>nd</sup> St., and E. 34<sup>th</sup> St. In addition, installation of a 48" trunk water main was performed along E. 35<sup>th</sup> St. b/w 1<sup>st</sup> Ave. and 2<sup>nd</sup> Ave. The city contractor continued utility work along E. 35<sup>th</sup> St. b/w 2<sup>nd</sup> Ave and the QMT Exit up to the SE corner of 3<sup>rd</sup> Ave. The city contractor continued support for Con Ed utility work along the east side of 1<sup>st</sup> Ave. b/w E. 34<sup>th</sup> St. and E. 36<sup>th</sup> St.

### Community Impacts

During construction hours, you can expect increased levels of dust, noise, and heavy equipment. In addition, vehicular lane closures or detours may occur. There may be limited curbside parking and you will be notified if certain bus stops will be moved. Please note, signs are posted where necessary and emergency vehicle/pedestrian/building access will be maintained at-all-times.

### Proposed Work Schedule: Third Quarter 2023

Permanent Restoration of 2<sup>nd</sup> Avenue between East 32<sup>nd</sup> Street and East 34<sup>th</sup> Street.

### Special Needs

Individuals with special needs who may be uniquely impacted by this project should contact the project's Community Construction Liaison, as soon as possible, to make them aware of your situation. DDC will work with you to attempt to minimize the inconvenience as much as possible.

The city contractor will continue utility work along East 35<sup>th</sup> Street b/w 2<sup>nd</sup> Avenue and the QMT Exit up to the southeast corner of 3<sup>rd</sup> Avenue. (Weekends only-8:00am-4:30pm). In addition, the city contractor will continue supporting Con Edison utility work along the east side of 1<sup>st</sup> Avenue between East 34<sup>th</sup> Street and East 36<sup>th</sup> Street.

### Community Construction Liaison (CCL)

The DDC has assigned Youseph Rasheed, as the Community Construction Liaison (CCL) for this project. Contact Youseph for your project related inquiries/concerns.

Phone: 646-768-9105


Email: [2ndAvenue.ccl@gmail.com](mailto:2ndAvenue.ccl@gmail.com)

Field Office: 300 E. 40th St., New York, NY

10016 Office Hours: Mon-Fri 7:00am-3:30pm

### DDC Video:

<https://www1.nyc.gov/site/ddc/projects/videos.page>

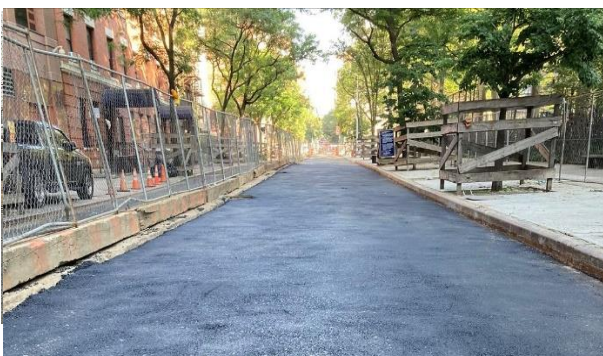

Restoration E. 35 / 1<sup>st</sup> – QMT Approach

### Newsletter Distribution

Distribution of Construction Newsletters for this project are within the footprint of the project & Manhattan's Community Board #6.
